MONTCEAU LES MINES LUCY (S109FB-SS)
IPS# 503648 - PROPOSAL SCHEDULE

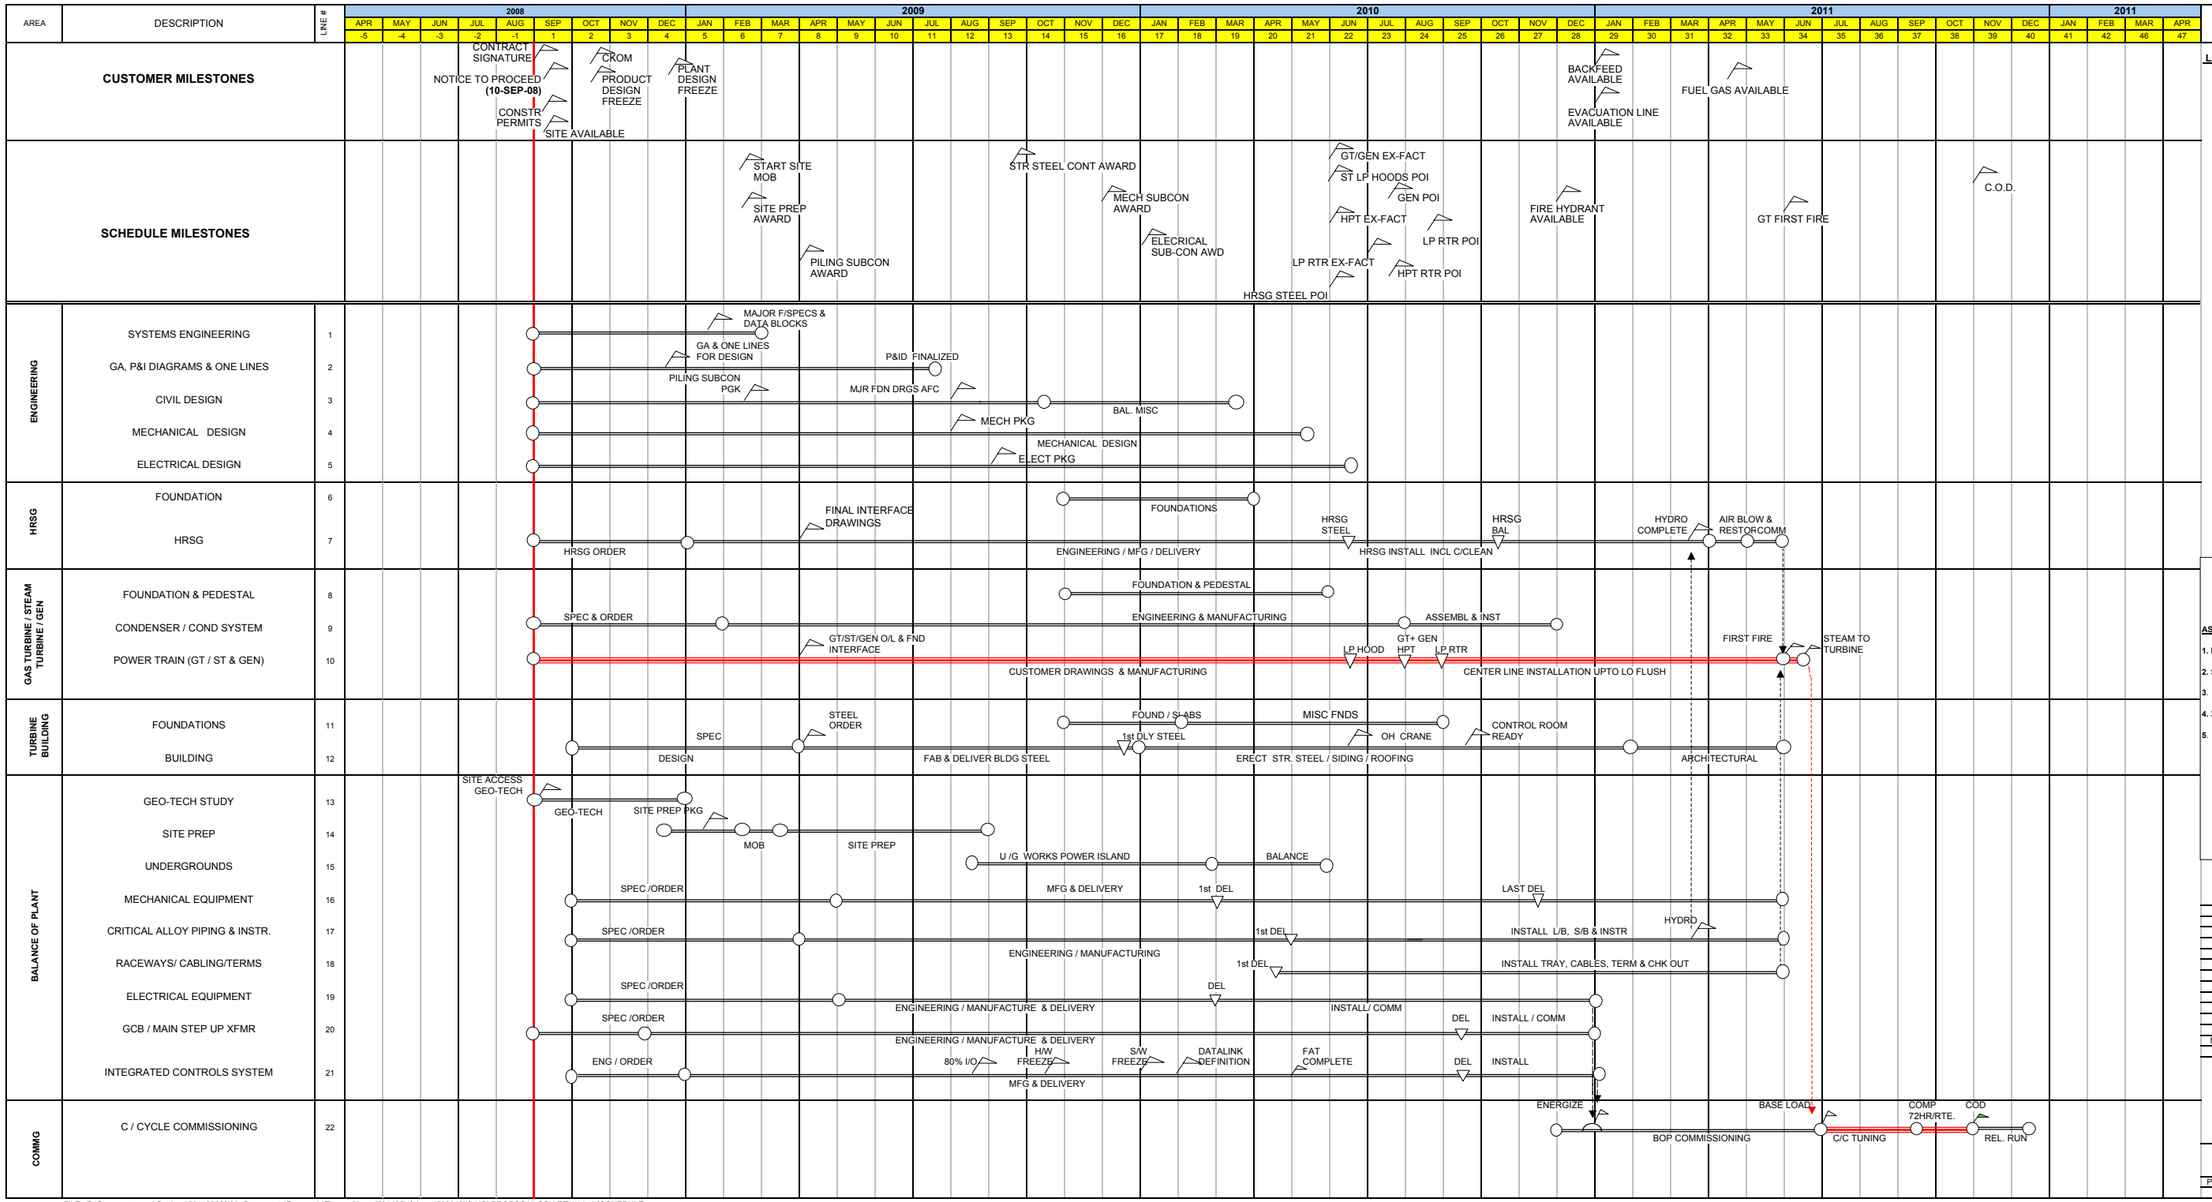

S109FB- SS
COMBINED CYCLE PROJECT

LEGEND:

- SCHEDULE MILESTONE EVENT
- SITE DELIVERY
- COMPLETED MILESTONE EVENT
- ACTIVITY
- CRITICAL ACTIVITY
- INTERDEPENDENCE
- CRITICAL INTERDEPENDENCE

ABBREVIATIONS:

NTP	NOTICE TO PROCEED
P&ID	PROCESS & INSTRUMENTATION DIAGRAMS
PREP	PREPARATION
SPECS	SPECIFICATIONS
HRSG	HEAT RECOVERY STEAM GENERATOR
COD	COMMERCIAL OPERATION DATE
MSD	MATERIALS SHIPPED DIRECT
CT	COOLING TOWER
BOP	BALANCE OF PLANT
ERB	ENGINEERING REVIEW BOARD
FAT	FACTORY ACCEPTANCE TEST
DEL	DELIVERY
GCB	GENERATOR CIRCUIT BREAKER
LB,SB	LARGE BORE , SMALL BORE

ASSUMPTIONS :

1. DESIGN FREEZE DEFINED IN CONTRACT
2. SUPPLIERS PRE- APPROVED IN THE CONTRACT
3. HRSG AND STEAM PIPES CLEANED BY AIR BLOWS
4. 30 DAY RELIABILITY RUN AFTER COD
5. NO CUSTOMER APPROVAL OF DRAWINGS OR CUSTOMER MFG HOLD POINTS

NO.	DATE	REVISION	CKD.
11	14-Apr-08	CL Installation - GT to FF 10m	DR
10	14-Apr-08	CL Installation - GEN to FF	DR
9	11-Apr-08	CL Installation	DR
8	09-Apr-08	ST EX-Factory	DR
7	28-Mar-08	ICS	DR
6	26-Mar-08	Revised NTP	DR
5	20-Dec-07	Contract Sig (6/20/08)	DR
4	18-Dec-07	Comments Added	DR
3	17-Dec-07	Comments Added	DR
2	12-Dec-07	Comments Added	DR
1	07-Dec-07	GT/ST/GEN New Dates	DR
0	05-Nov-07	Initial Issue	DR

cobra

S109FB-SS
LUCY PROPOSAL SCH

PROJECT NO.	SCHEDULE NO.	REV.
503648	PROPOSAL SCHEDULE	11

FILE :D:\Documents and Settings\501182869\My Documents\Proposals\Thermal\Lacq(701185) & Lucy(503648)\[LUCI PROPOSAL SCH REV-11.xls]SCHEDULE

PRINTED: 04/14/08 10:01 AM
